


Plateau Valley Medical Clinic

FCI Constructors Inc.

Schedule July 8, 2011

Activity ID	Activity Name	Original Duration	Start	Finish	2011						2012
					Jul	Aug	Sep	Oct	Nov	Dec	Jan
Plateau Valley Medical Clinic		207d	21-Mar-11	03-Jan-12							
Preconstruction/Design		94d	21-Mar-11	28-Jul-11							
A1810	Site for CDot	2d	21-Mar-11	22-Mar-11							
A2000	Site Final Deisgn	13d	21-Mar-11	06-Apr-11							
A2090	Building Schematic Design	11d	21-Mar-11	04-Apr-11							
A2010	Landscape Plan	20d	23-Mar-11	19-Apr-11							
A2040	Traffic Study - Hudson	21d	23-Mar-11	20-Apr-11							
A2050	Submit for CDOT	1d	31-Mar-11	31-Mar-11							
A2060	CDOT Review	45d	01-Apr-11	02-Jun-11							
A2100	Owner Review	3d	05-Apr-11	07-Apr-11							
A2110	Abatement assesment	11d	05-Apr-11	19-Apr-11							
A2120	Owner Meeting - SD Estimate Review	1d	05-Apr-11	05-Apr-11							
A2130	Design Development Drawings	32d	06-Apr-11	19-May-11							
A2020	Submit for Planning Clearance	1d	20-Apr-11	20-Apr-11							
A2030	Planning Clearance Application	50d	21-Apr-11	29-Jun-11							
A2140	DD Cost Estimate	10d	20-May-11	02-Jun-11							
A2070	Response to CDOT	7d	03-Jun-11	13-Jun-11							
A2150	Owner Meeting - DD Estimate Review	1d	03-Jun-11	03-Jun-11							
A2160	CD Drawings	23d	06-Jun-11	06-Jul-11							
A2080	2nd CDOT Review	20d	14-Jun-11	11-Jul-11							
A2170	CD Estimate	13d	07-Jul-11	25-Jul-11							
A2190	Submit for Building Permit	1d	07-Jul-11	07-Jul-11							
A2200	Building Permit Approval	14d	08-Jul-11	27-Jul-11							
A2180	Owner Review and Approval of GMP	3d	26-Jul-11	28-Jul-11							
Site Work and Improvements		126d	18-May-11	09-Nov-11							
A2220	Owner Vacate Main and 1st floor of old building	18d	18-May-11	10-Jun-11							
A2230	Temporary Walls on Main and 1st floor	3d	09-Jun-11	13-Jun-11							
A2210	Asbestos Abatement of Old Building	20d	20-Jun-11	15-Jul-11							
A2240	Disconnect utility for Demo	8d	18-Jul-11	27-Jul-11							
A1670	Demo Old Hospital Building	15d	28-Jul-11	17-Aug-11							
A1680	Surveying/Layout	5d	08-Aug-11	12-Aug-11							
A1690	Site Grading	20d	15-Aug-11	09-Sep-11							
A1720	Utility Services (Water, Sewer, Gas, Electric,)	19d	15-Aug-11	08-Sep-11							
A1700	Site Concrete Prep	5d	12-Sep-11	16-Sep-11							
A1730	Irrigation Sleeves	3d	16-Sep-11	20-Sep-11							
A1710	Pour Site Concrete	10d	19-Sep-11	30-Sep-11							
A1770	Site lighting	5d	19-Sep-11	23-Sep-11							
A1740	Road Prep	5d	03-Oct-11	07-Oct-11							
A1750	Place Asphalt	4d	10-Oct-11	13-Oct-11							
A1760	Irrigation system	5d	10-Oct-11	14-Oct-11							
A1780	Landscaping & Plantings	8d	17-Oct-11	26-Oct-11							
A1790	Deficiency List & Corrections	5d	27-Oct-11	02-Nov-11							

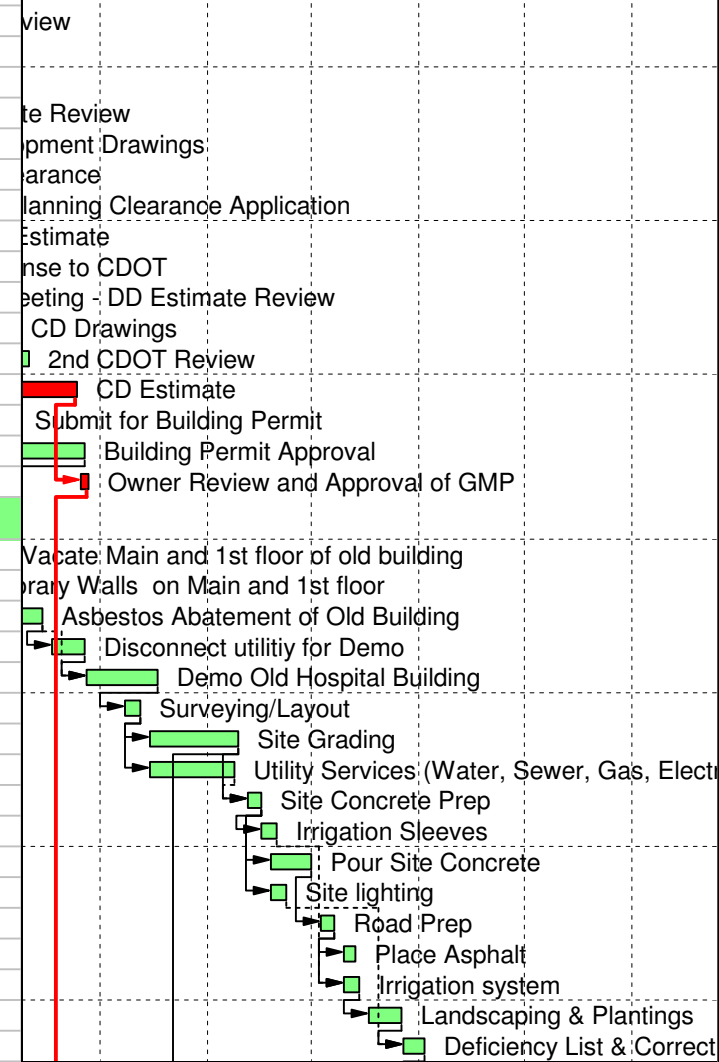

Activity ID	Activity Name	Original Duration	Start	Finish	2011						2012	
					Jul	Aug	Sep	Oct	Nov	Dec	Jan	
A1830	Plumbing and Electrical Underground	2d	31-Aug-11	01-Sep-11								
A1840	Form and Pour Slab on Grade	3d	02-Sep-11	06-Sep-11								
A1850	Interior and Exterior Framing and Roof Structure	6d	07-Sep-11	14-Sep-11								
A1860	Exterior sheeting and roof sheeting	5d	15-Sep-11	21-Sep-11								
A1870	Roofing	3d	22-Sep-11	26-Sep-11								
A1880	MEP Roughin	3d	22-Sep-11	26-Sep-11								
A1930	Windows and Door Frames	2d	22-Sep-11	23-Sep-11								
A1890	Insulate and Hang Tape and Finish Sheetrock	6d	27-Sep-11	04-Oct-11								
A1920	Exterior Skin	8d	27-Sep-11	06-Oct-11								
A1900	Paint	3d	05-Oct-11	07-Oct-11								
A1910	Lighting and electrical Trim	2d	10-Oct-11	11-Oct-11								
A1940	Flooring	3d	10-Oct-11	12-Oct-11								
A1950	Plumbing and mechanical Trim	1d	13-Oct-11	13-Oct-11								
A1960	Deficiency List and Corrections	3d	14-Oct-11	18-Oct-11								
A1970	Punch List and Corrections	3d	19-Oct-11	21-Oct-11								

